


SHOP BILL

LINE NO.	SHIPPING LIST		PCS REQD	DESCRIPTION		LENGTH		ASSEMBLY MARK	REMARKS	MTRL. SPEC.	MATERIAL APPLICATION	
	NO.	MARK		SYMBOL	SECTION DIM'S	FEET	INCHES				P.O. NO.	LINE NO.
1												
2												
3	1	151M1		SLAB SUPPORT BRACKET								
4			1	PL 1/2 x 42	3	4	A			M270-50 SHN		
5			1	PL 1 x 8	3	5	C			M270-50 8328IS	1	
6			1	PL 1 x 8	5	4 3/4	D	BEND		M270-50 8328IS	1	
7												
8												
9												
10												
11												
12												
13												
14												
15												
16												
17												
18												
19												
20												
21												
22												
23												
24												
25				DOMESTIC MATERIAL								

SEE HN101 FOR FABRICATION NOTES

PAINT NOTE "C" APPLIES TO ALL OPEN HOLES AT BRACKET.

PDC Sample DWG 304
 FREEPORT BRIDGE ~ PA
 HIRSCHFELD INDUSTRIES
 BRAYMAN CONSTRUCTION CO.
Slab Supp Bracket Det.
 PENNDOT 2010

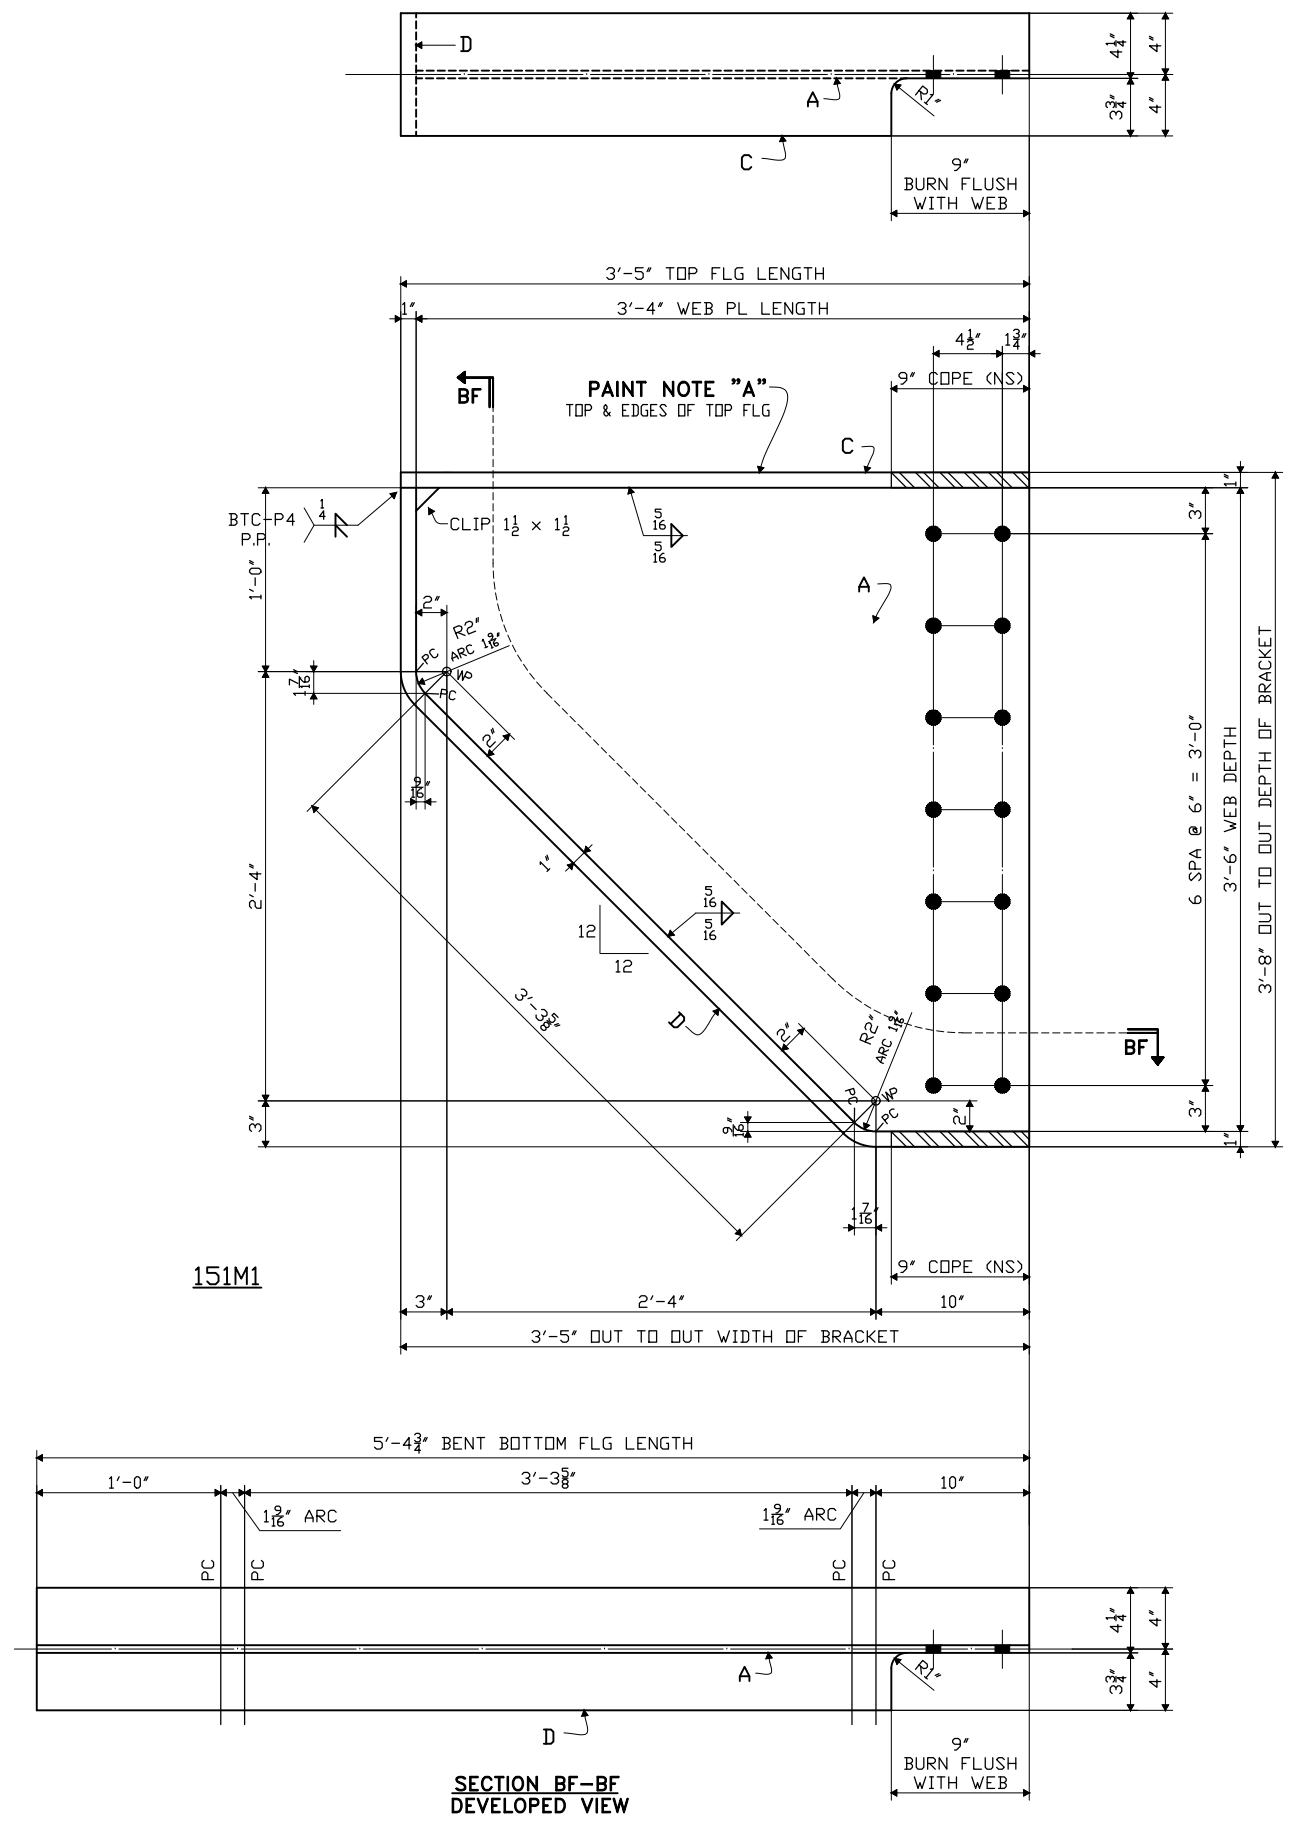

PADDT EMCS 75586
 S.R. 0356 SECTION 06M
 NB: SEG. 0222 OFFSET 1031
 SB: SEG. 0223 OFFSET 1031
 STRUCTURE No. S-29745 -N. APPROACH
 STA: 1956+44.90 TO STA: 1965+39.90

FABRICATED BY COLFAX
 HOLES - 15/16" SHOP FASTENERS
 SHOP PAINT PAINTED PER HN101 & AS NOTED
 SHOP INSPECTION
 GENERAL NOTES

REVISIONS		
DATE	NO.	BY
	R1	

ORDER NO. 10-18679H22
 DETAILS OF SLAB SUPPORT BRACKET
 NORTH APPROACH -NORTHBOUND LANE
 PROJECT S.R. 0356 (FREEPORT BRIDGE)
 STA: 1951+08.15 OVER ALLEGHENY RIVER
 LOCATION ALLEGHENY, WESTMORELAND & BUTLER CO'S, PA
 CUSTOMER BRAYMAN CONSTRUCTION CO.
HIRSCHFELD INDUSTRIES
 BRIDGE
 GREENSBORO, NC (336) 275-9711
 MADE BY WS
 CHECKED BY PDC/SB
 SQUAD LEADER Precise Drafting Co, Inc.
 DATE 09-2010
 SHEET HF151
